



PROJECT PLANNING PACKAGE · 2026–2027

Marianella Training Center Renovation

Merging innovation and sustainability to elevate youth and senior player development for the club in Naples.

Eduardo Enriquez · Simone Ferrieri · Steven Le · Paul Le Gall

Project Managers | Budget \$300,000 | July 2026 – April 2027

Project Charter

1

The foundation: purpose, scope, and authority for the one-year planning effort.

KEY MESSAGE A renovation that brings innovation and sustainability while improving the quality of sport and player health across the youth academy and the official team.



Purpose

Provide a quality training facility for youth player development that merges innovation and sustainability.



Objectives

Evaluate the space and demolition plans, estimate the budget, present a report, and render the final design in 3D.



Scope & Boundaries

Plan a larger, renewable-energy facility with enough fields and full daytime staff. Planning only — within current land.



Deliverables

3D renderings, a project report and presentation, and signed permits — all within \$300,000.

Work Breakdown Structure

2

Six phases decomposing the full scope of work, July 2026 – April 2027.

1.0

Project Initiation

Charter, stakeholders & authorizations, preliminary budget, schedule, risk register.

2.0

Site Assessment & Evaluation

Demolition survey, land & infrastructure checks, sustainability audit, data package.

3.0

Design & Planning

Master plan, renewable-energy features, fields, staffing, draft specs & budget refinement.

4.0

Permits & Regulatory Approvals

Regulations research, permit applications, legal/zoning, signed permits & approvals.

5.0

Final Deliverables & 3D Renderings

Final plan set, 3D renders, project report, final presentation & delivery package.


6.0

Project Closeout

Stakeholder sign-off, lessons learned, complete project archive.

Stakeholder Register

20 stakeholders mapped by influence and interest to guide engagement.

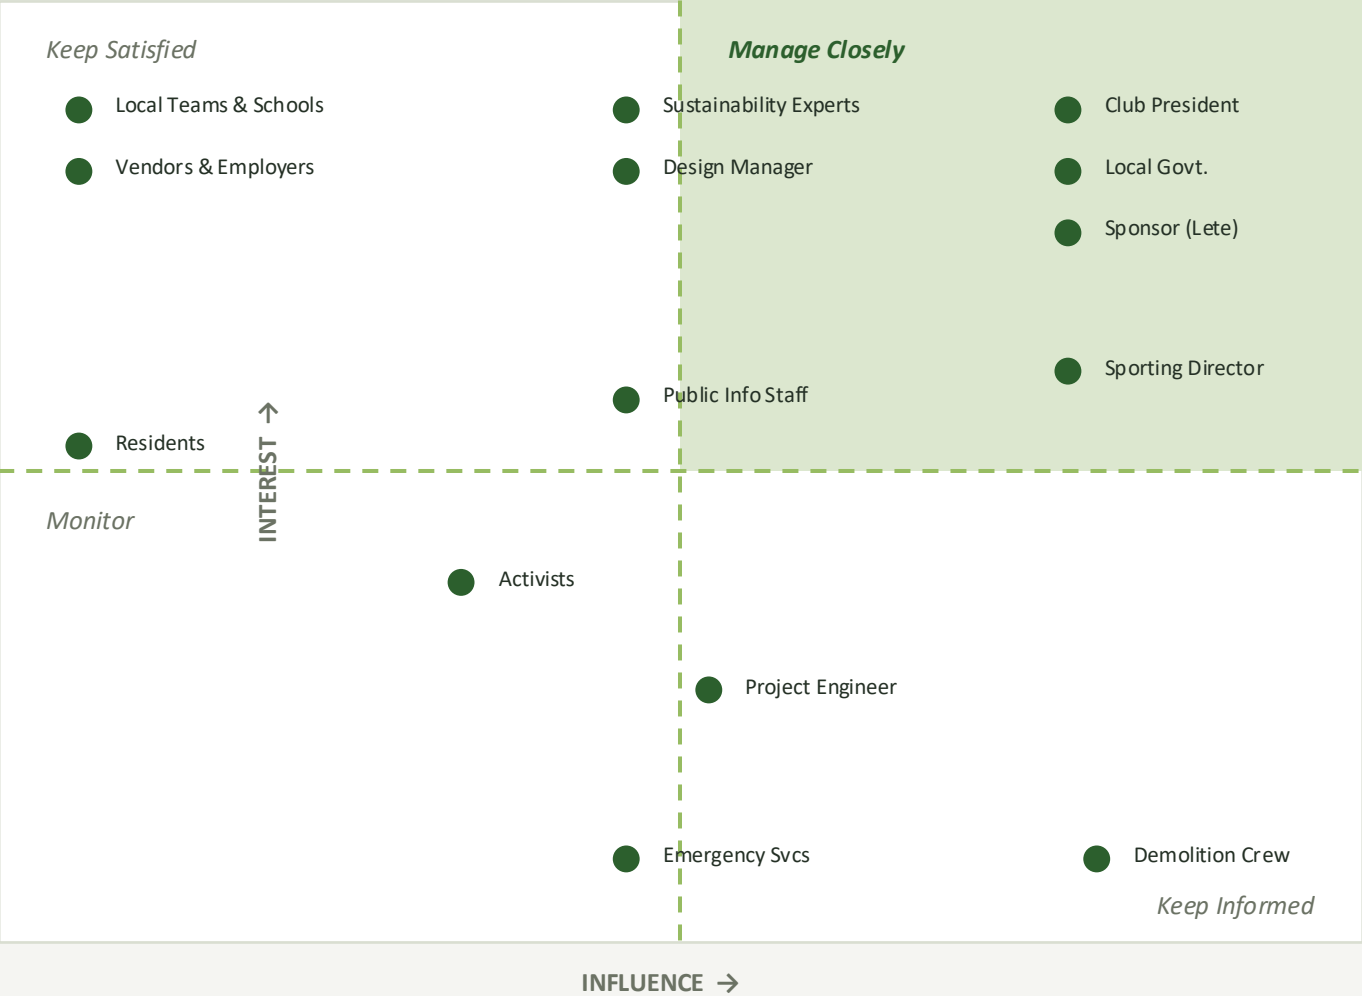

Sponsors & Governance

Club president, local government, Lete — high influence, high interest.



Project Team

Sustainability experts, design manager, engineers, PR & social media.



End Users & Community

Local teams, schools, residents, employers, vendors, public figures.




Watch Closely

Residents (opposed) and activists (mixed) need careful engagement.

Schedule / Gantt Chart

Six phases across 421 days, with four key milestones (M1–M4).

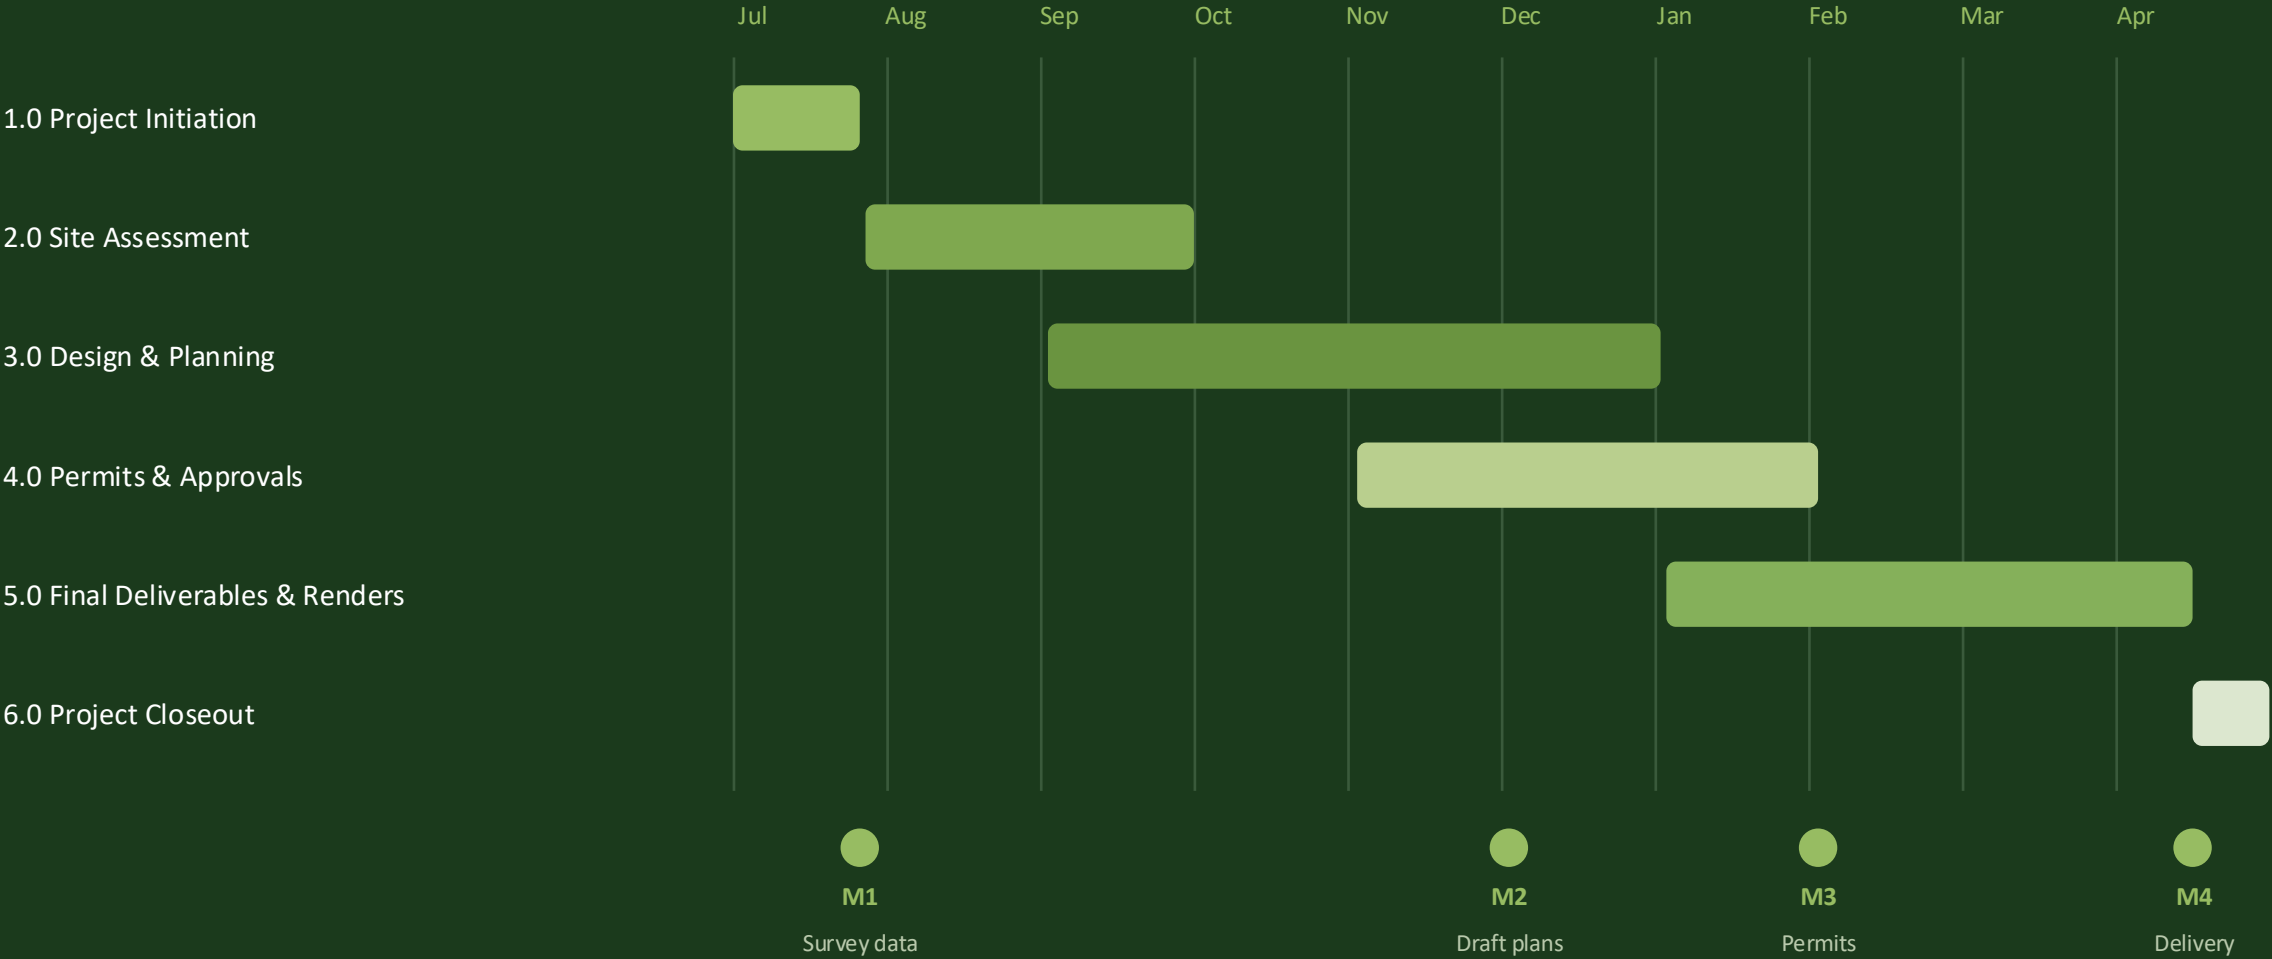

M1 Jul 2026 · M2 Oct 2026 · M3 Jan 2027 · M4 Apr 2027

Budget

\$300,000 distributed across six phases, with a contingency reserve.




- Initiation
- Site Assessment
- Design & Planning
- Permits
- Final Deliverables
- Closeout
- Contingency

Phase	Budget	%
Project Initiation	\$14,900	5.0%
Site Assessment & Evaluation	\$43,000	14.3%
Design & Planning	\$103,450	34.5%
Permits & Regulatory Approvals	\$30,300	10.1%
Final Deliverables & 3D Renderings	\$73,800	24.6%
Project Closeout	\$14,000	4.7%
Contingency Reserve	\$20,550	6.9%
TOTAL	\$300,000	100%

Risk Register

15 risks scored by impact × probability; highest-priority risks shown with mitigations.

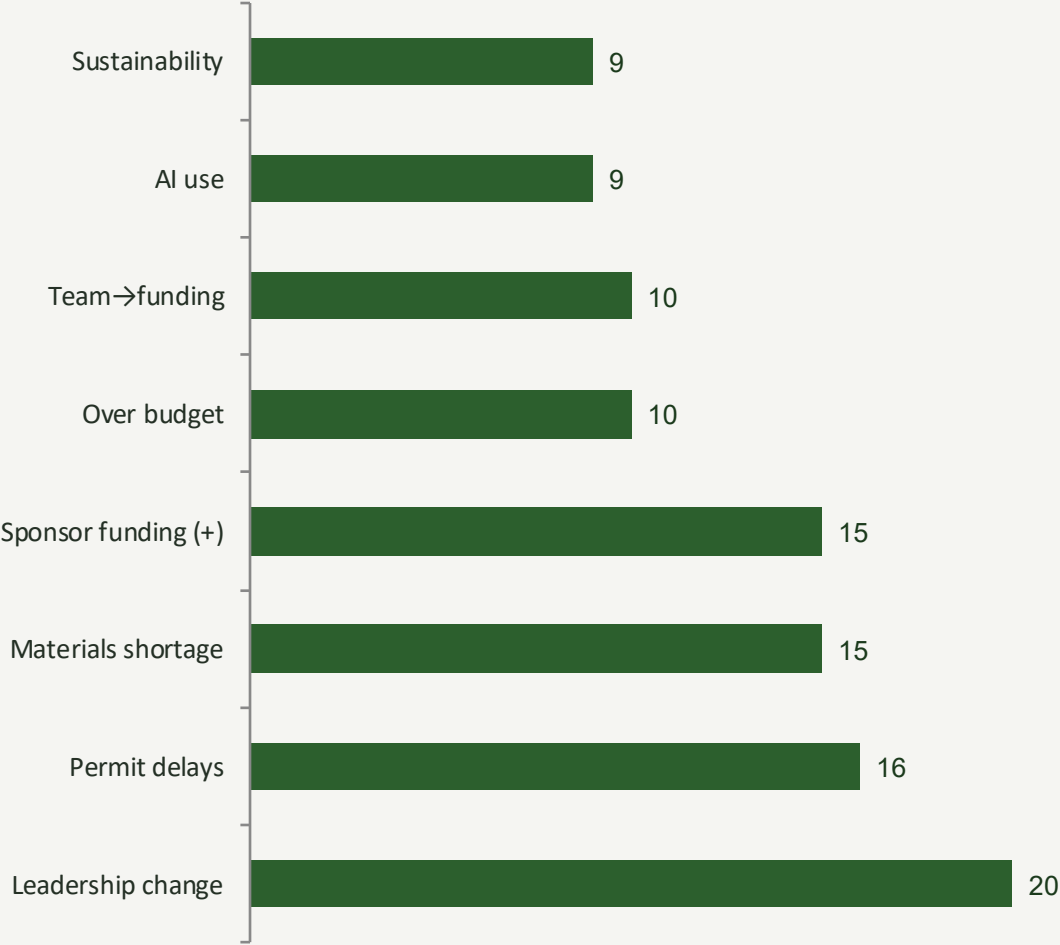

Leadership change (20)

Document progress; hold regular meetings.

Permit delays (16)

Adjust the iron triangle to current rules.

Materials shortage (15)

Source alternative materials.

Over budget (10)

Plan & monitor the full project lifecycle.

Communications Plan

7

Who hears what, how, and how often — escalating when SPI/CPI drift from 1.0.



Team Meeting Notes

Weekly · Project team

Takeaways shared via email / Word doc.



General EVM Report

Weekly · Project team

EVM curve summary; escalate if SPI/CPI $\neq$ ~1.



In-Depth EVM Report

Monthly · Team, owner, sponsors, govt.

Full PPT of evaluations; loop in leaders.



Important Update Emails

As needed · Project team

Bulleted critical changes, not paragraphs.



Project Kickoff

Once (start) · Team & sponsor

Scope, roles, milestones, resource review.



Mid-Project Status

Once (midpoint) · Project team

Research, budget progress, layout check.

Performance Metrics Plan

8

What is measured, how, and the tolerances that trigger action.



Schedule Adherence

Shared calendar, weekly review

Tolerance: Max 3-day internal slip; 0-day on client dates.



Budget Accuracy

Cost estimation & bi-weekly review

Tolerance: Baseline within agreed % of market averages.



Sustainability Integration

Green-feature checklist

Tolerance: Zero tolerance — eco-features must be present.



3D Render Quality

High-res export tests

Tolerance: HD; no texture overlap or glitches.



Scope Control

PM tracks triple constraint

Tolerance: Scope changes only by unanimous agreement.



Deliverable Quality


Inspector checklist per phase

Tolerance: Must pass safety & quality or be redone.

Planned Value Curve

9

Time-phased cumulative budget (BCWS) — the baseline for earned-value tracking.

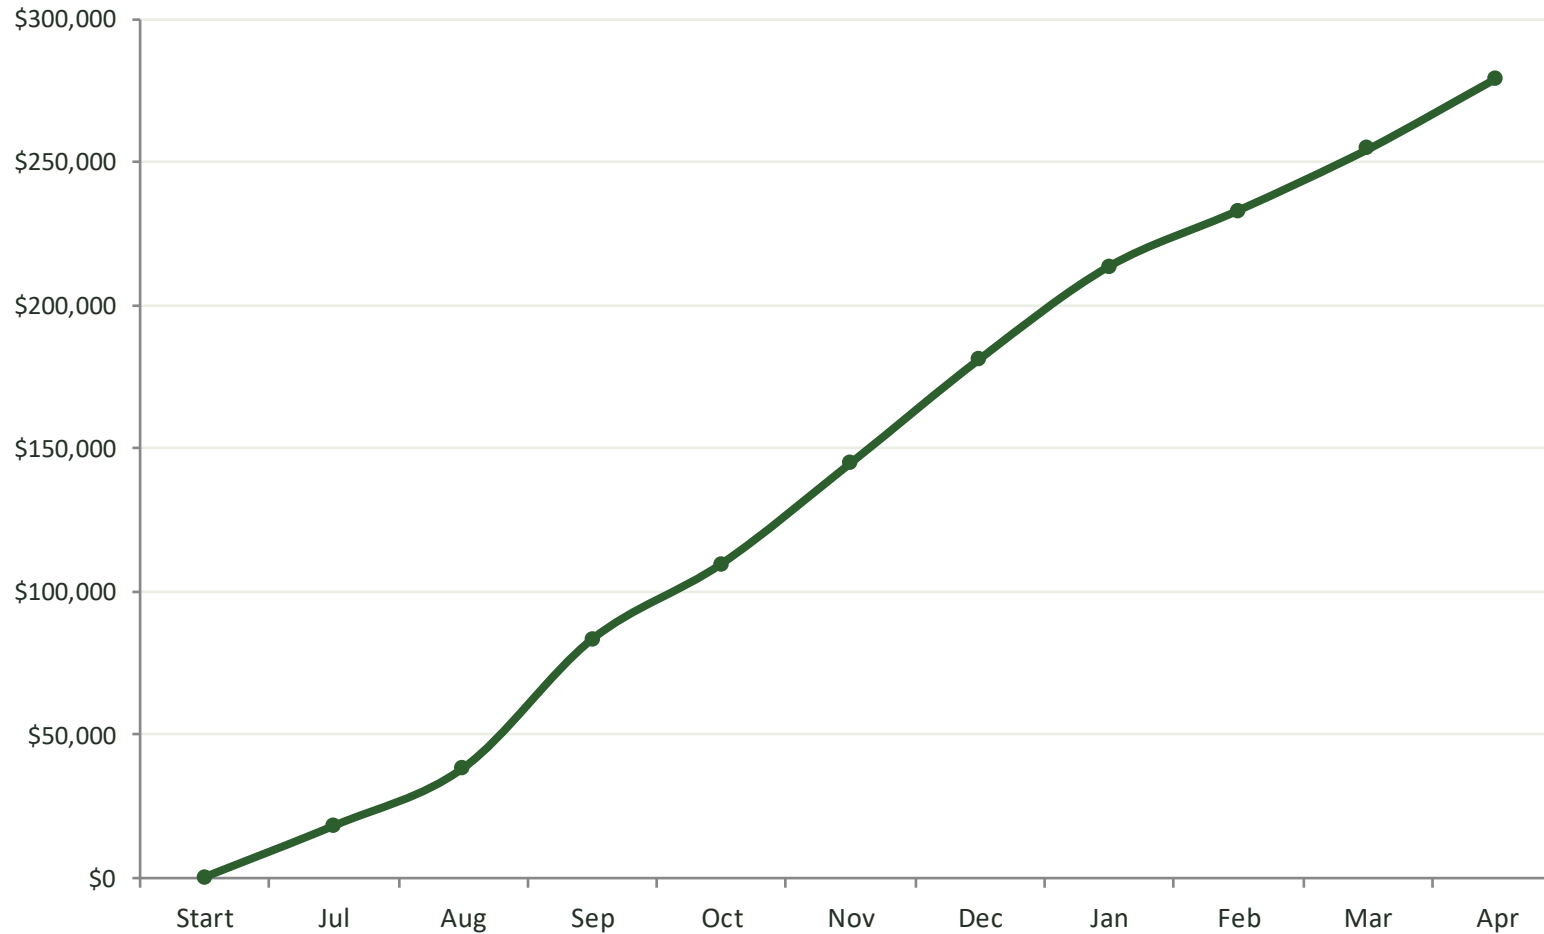

S-curve shape

Spend accelerates through the design-heavy middle months (Sep–Dec).

Baseline total

Curve accumulates to \$279,450 — the allocated phase budget.

Contingency held

\$20,550 reserve sits outside the baseline (standard EVM practice).

Delivery & Closure Plan

10

Handing a complete, permit-ready package to the execution team.



Team Transition

Planning team formally hands over all artifacts, designs, and documentation to the execution team, then is released from the project.



Socialization Plan

Secure buy-in through facility previews, joint staff onboarding, and feedback loops so the hub is embraced as sustainable from day one.



Artifacts Saved

All 11 deliverables archived with Project Manager sign-off; no external vendors — handled entirely by the internal team.

Deliverables Signed Off

- ✓ Project charter
- ✓ WBS
- ✓ Stakeholder register
- ✓ Schedule / GANTT chart
- ✓ Budget
- ✓ Risk register
- ✓ Communications plan
- ✓ Performance metrics plan
- ✓ Planned value curve
- ✓ Delivery & closure plan
- ✓ Group presentation

Next phase: 3D renders & blueprints handed to the execution team.



The End

A complete, permit-ready planning package for the Marianella Training Center — sustainable, innovation-driven, delivered within \$300,000 and on schedule.

Eduardo Enriquez · Simone Ferrieri · Steven Le · Paul Le Gall

Marianella Training Center Renovation · July 2026 – April 2027
